Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Name: Divisha Gupta


SRN: PES1UG24CS158

Section: C

1. Jira Backlog: Epics and User Stories

The backlog was organized into three functional Epics: Report Lost Baggage, Track Baggage, and Baggage Recovery and Notifications. The user stories were linked to their respective parent Epics.


Jira backlog showing Epics, Sprint 1 stories, and backlog stories.

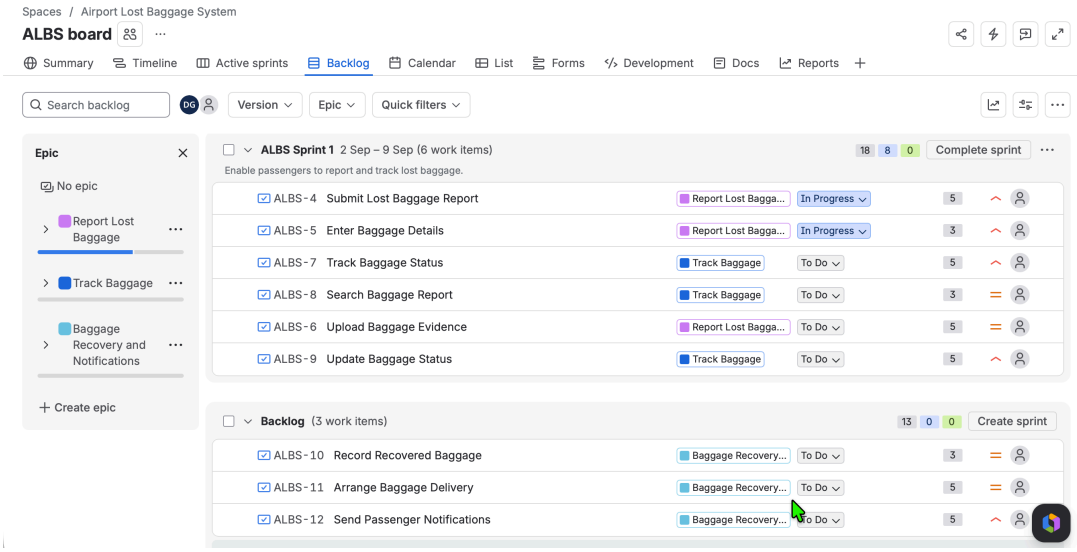


2. Priorities and Story-Point Estimates

Story points were assigned using Fibonacci-style estimates (3 and 5 points) based on relative complexity, effort, and uncertainty. Higher-priority stories were selected first for Sprint 1.

Jira backlog showing story-point assignments and Epic relationships.

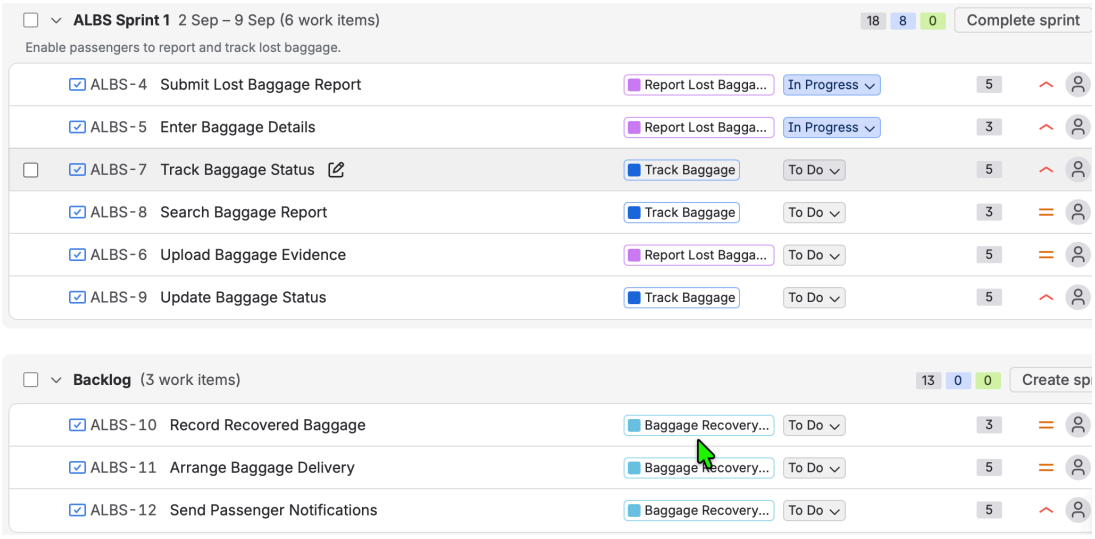


Sprint 2

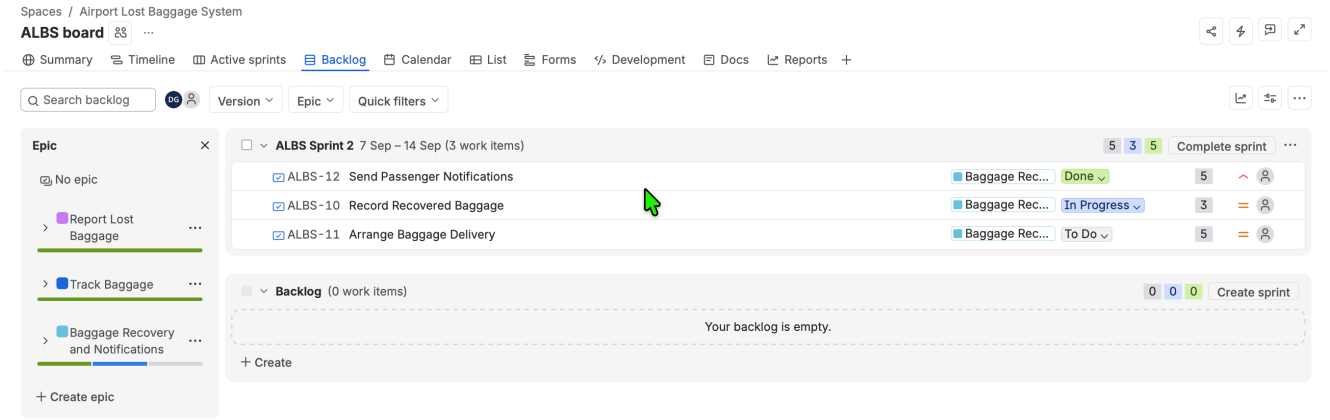


3. Sprint Board and Progress


Sprint 1 was planned with six stories and a goal of enabling passengers to report and track lost baggage. Stories were progressed through To Do, In Progress, and Done. The sprint was completed with all six stories in Done.

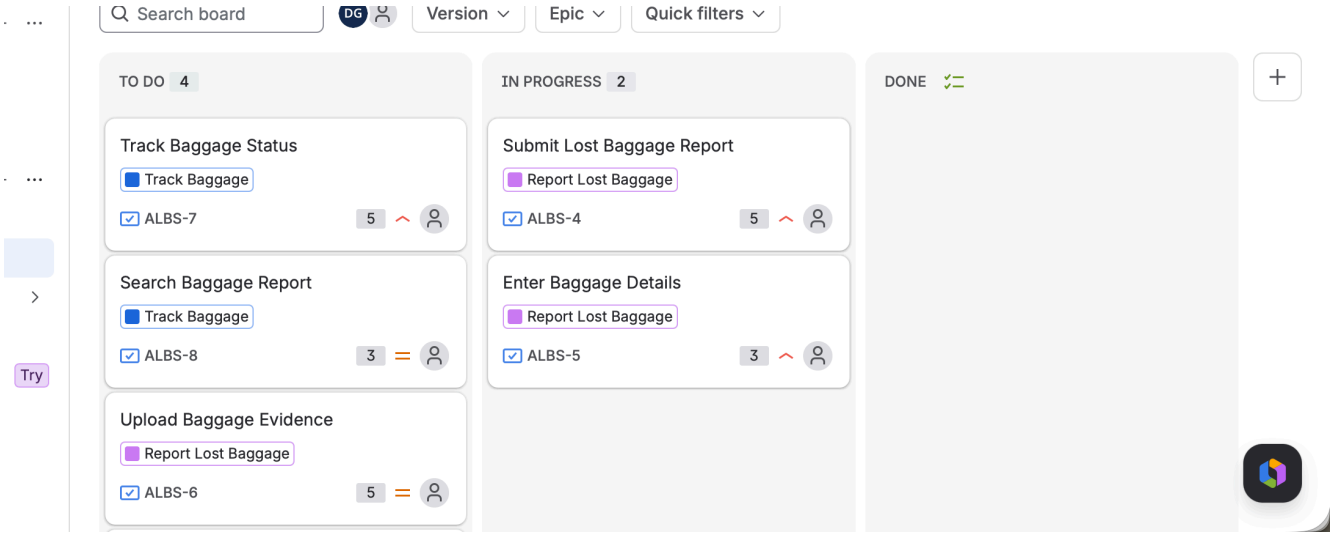


Sprint 1 board after all six stories were completed.

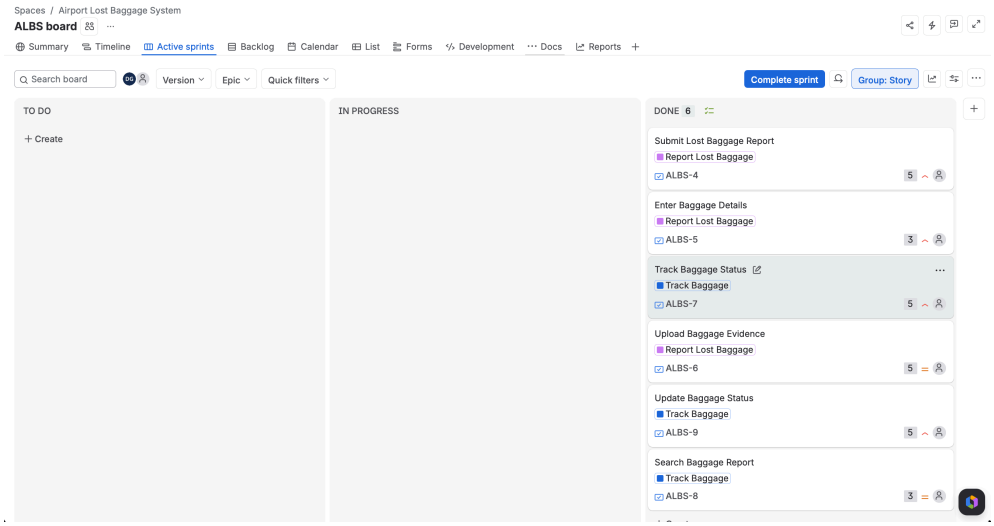

Sprint 2

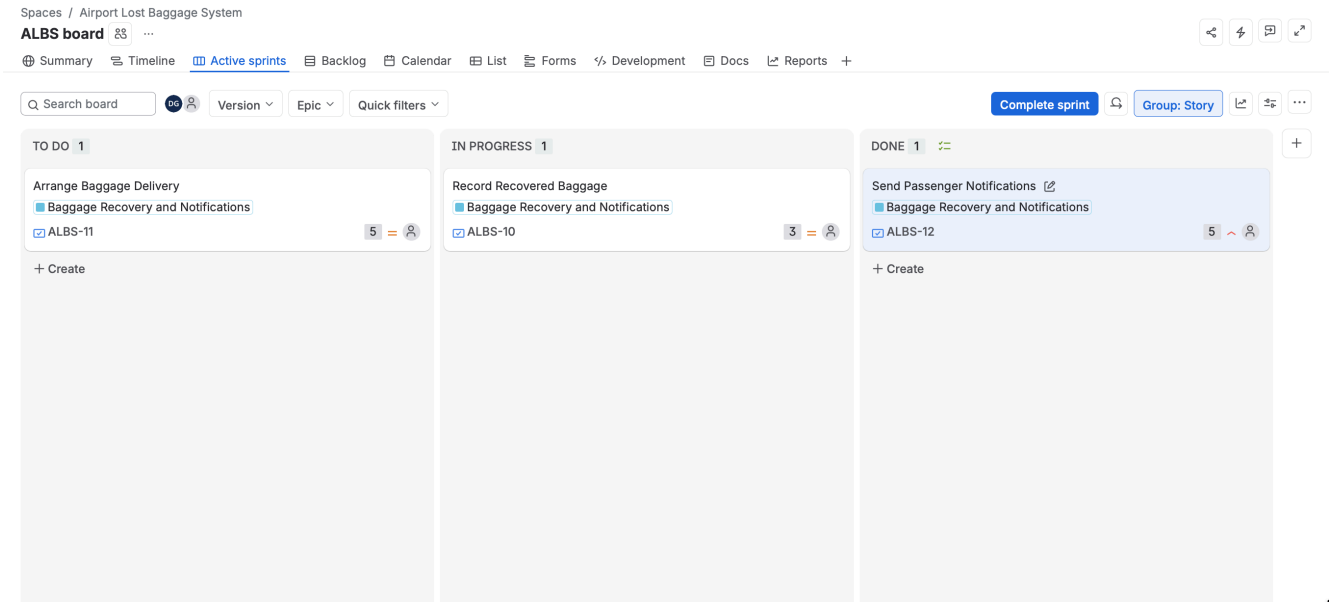


Sprint 2 board after all three stories were completed.

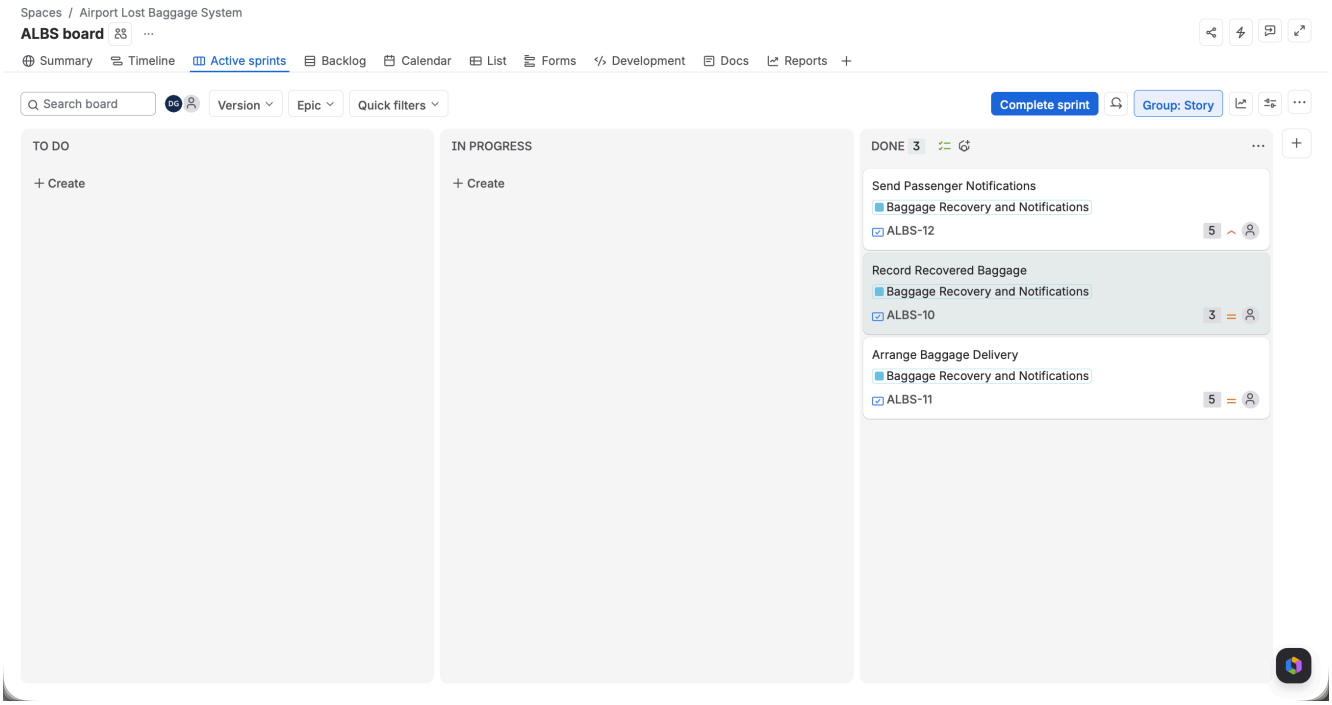


4. Burndown Chart

The red Remaining Values line shows the actual reduction in work from 26 story points to 0. The guideline is Jira's ideal reference line. It appears irregular because estimates were added after the sprint had already started.

Sprint 1 Burndown Chart.

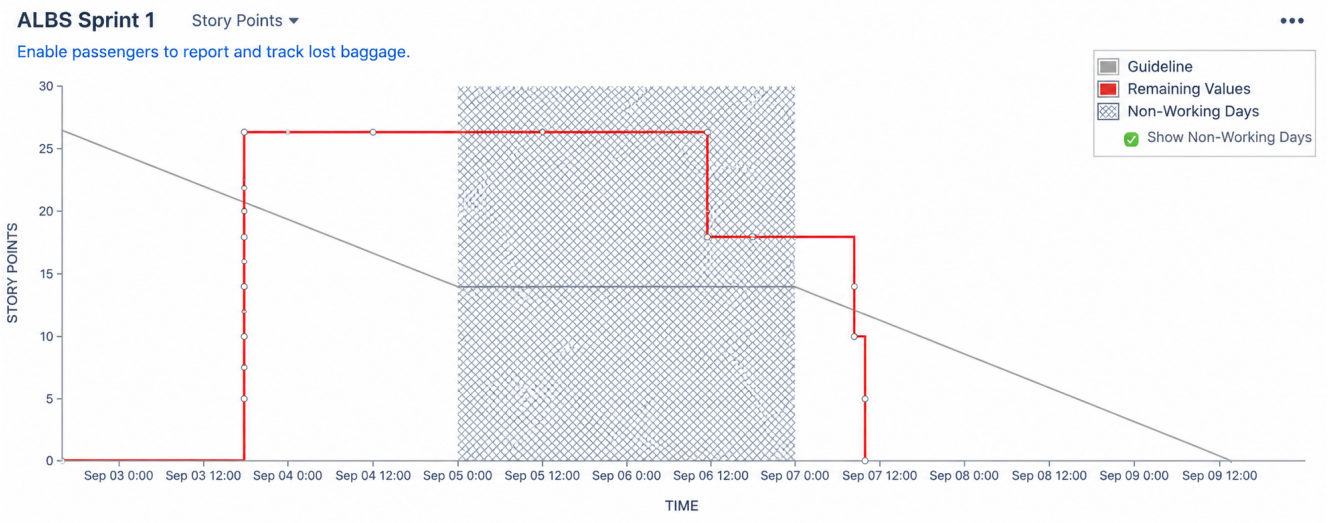

Sprint 2 Burndown Chart

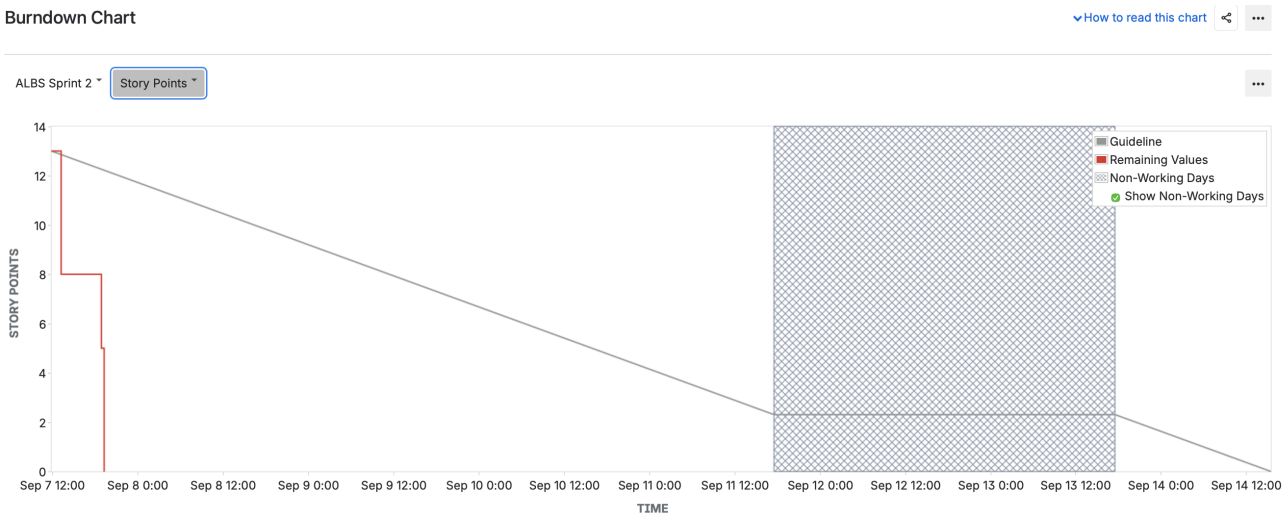

5. Reflection Questions

1. Did the estimations reflect the actual effort?

The story-point estimates provided a reasonable relative comparison of effort. The 3-point stories represented smaller and more focused features, while the 5-point stories involved greater functionality, processing, and uncertainty. Since this was a simulated sprint, the estimates could not be compared with actual development hours. However, all 26 planned story points could be completed in Sprint 1, suggesting that the selected workload was achievable. The use of Fibonacci-style values also helped distinguish between simpler and more complex stories.

2. Was the backlog well-prioritized?

Yes, the backlog was prioritized according to user value and functional dependency. The core passenger workflow was given higher priority: submitting a lost-baggage report, entering baggage details, tracking baggage, and searching for a report. These features form the main interaction flow of the system. Evidence upload and baggage-status updates were also included because they support the reporting and tracking process. Recovery, delivery, and passenger-notification features were placed in Sprint 2 because they depend on the initial baggage-reporting and tracking functionality being available.

3. How did the simulated sprint align with the plan?

The simulated work generally followed the planned Scrum process. The backlog was divided into Epics and User Stories, story points and priorities were assigned, and selected stories were placed into Sprint 1. The stories were then moved through To Do → In Progress → Done, and the sprint was completed with all six stories finished. Sprint 2 was subsequently created using the remaining recovery and notification stories. The main deviation was that the Sprint 1 story-point estimates were entered after the sprint had already started. Jira therefore treated them as scope changes, causing the ideal guideline in the burndown chart to appear irregular.

4. What insights did the burndown chart give about team capacity?

The burndown chart showed successful completion of all 26 story points planned for Sprint 1. It also showed that progress occurred in stages rather than all work being completed simultaneously. The chart highlighted the difference between actual progress and ideal progress: the red line represented the remaining work, while the guideline represented the expected linear reduction. Overall, the completed 26 points provide an approximate measure of the team's simulated capacity and can help plan a realistic workload for future sprints.

******
